


PO BOX 4235 MANDURAH NORTH WA 6210 Tel: +61 8 9524 6600 Mob: +61 409 115 517 Email: admin@cablelocates.com.au CLIENT: Zak, LD Total SITE ADDRESS: Napolean St, Cottesloe DATE: 22/5/18 SERVICE STATEMENT #: 11901 PLAN#: 1/1

Location Tech: Shane.H

No

Services as per DBYD

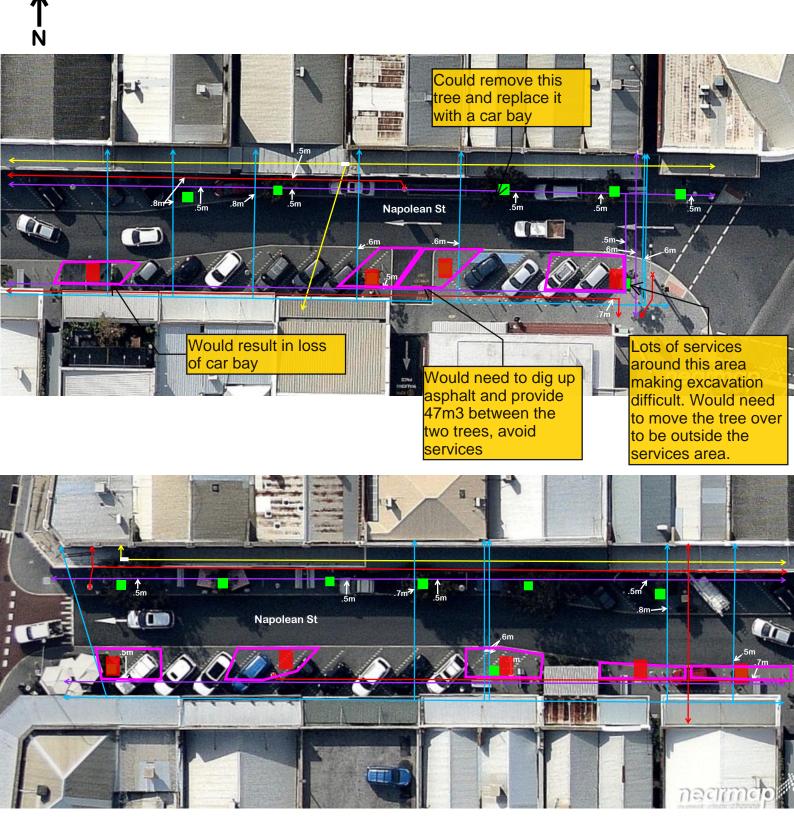

Legend:	
Power	
Telstra/NBN	
Unknown	
Water	

Tree 📕 Light X Note: All depths on plan are electronic only and are to be used as a guide only. Note: Crossings and closest parallel service marked to each tree only.

Note: Some pits Could not be opened as cars parked on them. These are not apart of $\ensuremath{\mathsf{DBYD}}$

)	Ð	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	Qtr 1, 2018 Qtr 2, 2018 Qtr 3, 2018 Qt Jan FebMarAprMayJun Jul AugSepOc	r 4, 2018 Qtr 1, 2019 Qtr tNovDec Jan FebMarAnn	2, 2019 Qtr 3, 2019 Qtr 4, 2019 Qtr 1, 2 1ayJun Jul AugSepOctNovDec Jan Feb	2020 Qtr 2, 2020 Q MarAprMay Jun Ju
1			Napoleon Street Tree Replacement Project	921 days	Tue 27/11/18	Tue 7/06/22		0%			1		<u>man prindjouri</u> je
2		-	Approvals	41 days	Tue 27/11/18	Tue 22/01/19		0%			P1		
3		-	OCM - approval of species and timeframe/purchase of trees	0 days	Tue 27/11/18	Tue 27/11/18		0%			♦ 27/11		
4		-5	Purchase trees (to remain at nursery)	1 wk	Wed 28/11/18	Tue 4/12/18	3SS+1 day	0%					
5			Christmas and January - break	7 wks	Wed 5/12/18	Tue 22/01/19	4	0%					
6			Tender	46 days	Wed 23/01/19	Wed 27/03/19	ni e a fin in se i I	0%			······		
7		-	Prepare tender documents (based on previous ones)	1 wk	Wed 23/01/19	Tue 29/01/19	5	0%			к,		
8			Advertise on Tenderlink	3 wks	Wed 30/01/19	Tue 19/02/19	7	0%					
9		-	Tenders close	0 days	Tue 19/02/19	Tue 19/02/19	8	0%			\$ 19/02		
10		-	Tender assessment	1 wk	Wed 20/02/19	Tue 26/02/19	9	0%			F		
11		-	Write council report for March OCM to award tender	2 days	Wed 27/02/19	Thu 28/02/19	10	0%					
12			Briefing Forum	0 days	Tue 5/03/19	Tue 5/03/19		0%			♦ 5/03		
13		-	Agenda forum	0 days	Tue 19/03/19	Tue 19/03/19		0%			19/	03	
14	1	-	Ordinary Council Meeting	0 days	Tue 26/03/19	Tue 26/03/19		0%			26,	/03	
15		-	Award contract	0 days	Wed 27/03/19	Wed 27/03/19	14SS+2 days	0%			▶ 27	/03	
16		-	Construction Works	833 days	Fri 29/03/19	Tue 7/06/22		0%					
17		.	Preliminaries, design work and set up	4 wks	Fri 29/03/19	Thu 25/04/19	15SS+1 day	0%					
18		-	Remove trees on south side	1 wk	Fri 26/04/19	Thu 2/05/19	17	0%					
19			Plant 9 trees on south side	2 wks		Thu 16/05/19		0%					
20		-	Remove trees on north side	1 wk	Fri 17/05/19			0%					
21		- ,	Install one new car bay	3 days	Fri 24/05/19			0%				•	
22			Plant 6-7 trees on north side (assuming claret ash)	2 wks	Wed 29/05/19			0%	1 m 1 m m m				
23			Practical Completion	0 days	Tue 11/06/19	Tue 11/06/19	22	0%				11/06	
24			Demobilisation		Wed 12/06/19			0%				¥ 11/00	
				1 day									
25			Defects period	156 wks	Wed 12/06/19		22	0%					
26		-	Future Works	120 days	Wed 12/06/19			0%				1	
27		-	Monitor Trees and street aesthetics	4 mons	Wed 12/06/19	Tue 1/10/19	22	0%					
28		-	Investigate relocating street furniture	1 mon	Wed 2/10/19	Tue 29/10/19	27	0%					
29		•	Planter boxes investigation, design and installation	2 mons	Wed 2/10/19	Tue 26/11/19	27	0%					
30		-	Vines investigation, design and installatio	n 2 mons	Wed 2/10/19	Tue 26/11/19	27	0%					
		oot Progra 3/10/18	Split		-	1 Ina	active Milestone active Summary	an ana ara-taon	Duration-only Manual Summar		only]	External Milestone Deadline	♦
			Milestone 🔶	Inactive Ta	SK	Ma	anual Task		Manual Summar	y Extern	al Tasks	Critical	

tr 3, 2020 0	2tr 4, 2020	Qtr 1, 2021 Q Jan FebMarAr	tr 2, 202	Qtr 3, 20	21 Qtr 4,	2021 Qt	r 1, 2022	Qtr 2, 2022
TAUGSEDO	ctnovDec	Jan FebMarAp	orMayJun	Jul Augse	<u>ep/OctNo</u>	<u>vDecJan</u>	FebMarA	prMayJun J
				N Strategy				
	Critical S Progress							
	1 TOQIC33							
